


GAS ASBL Address: 101 Cable Rd. Swanville 13260 2010
 Property: 9-19 L/S
 WO: 13- SC - SW - 81 - SWS - 5037 -

White Flag

Flagged 9/5 C.S.

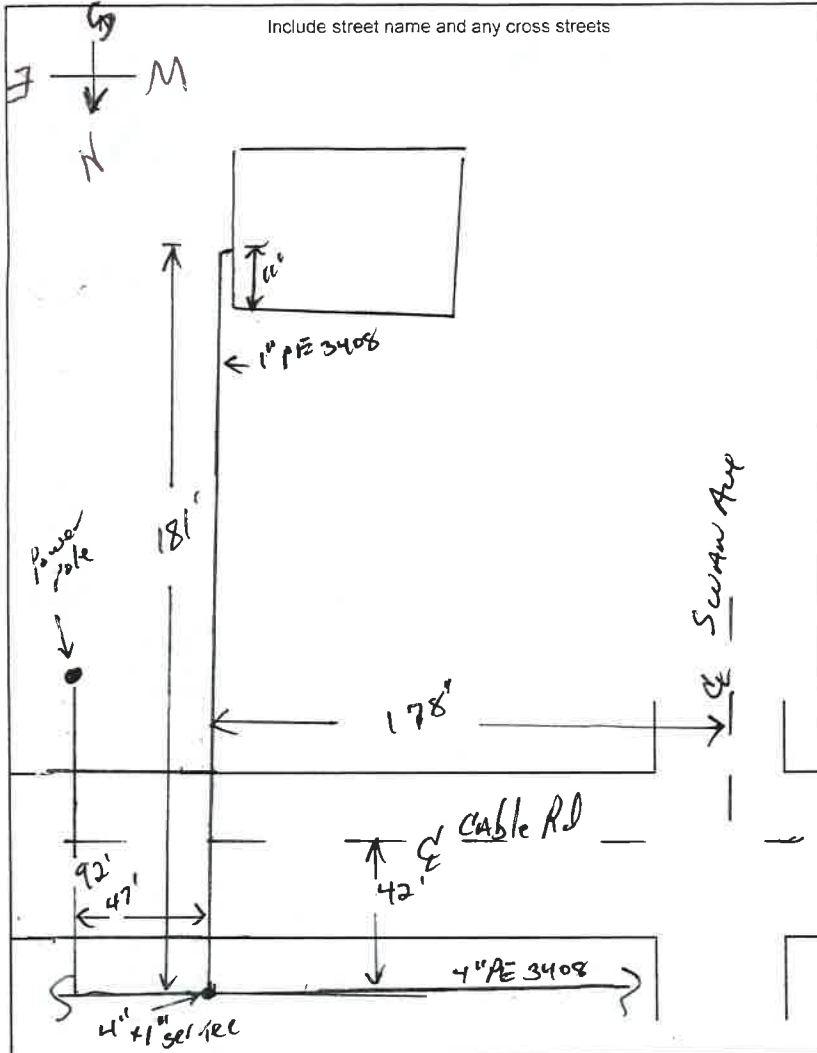

Remarks:

Material List	Lot #	Qty
Pipe 5/8" or 1"	NAD164033GA 17	181'
Tee 2x5/8 or 2x1		
Tee 4x5/8 or 4x1	298595	1
Tee 6x5/8 or 6x1		
EFV 5/8 or 1"	13171	1
5, 10 or 12 # Meter Bar		1
Cplg 5/8 or 1" or 2"	2	Bracket - post Foundtn.
Split Bolt	2	Riser 5/8 or 1"
5/8 or 1" ELL		Cap 5/8 or 1"
PE Tee 5/8 or 1"		PE Reducer 5/8x1"
Scrap 1" pipe		10'
Scrap wire		10'
wire		183'
Carsonite	Anode 3#	
# of Heaters	Restoration Y N	

Meter	
Locked ☐	Unlocked ☒ (E)
Size 275	Location Left
MFG Sensus	Reading 0000
New Meter # 18171/50	
Reg. Type/Press. 2#	5# 10# 12#
Old Meter#	
Old Meter Reading	

Does Winter Construction Apply? Y ☐ N ☐

Condition of Existing Pipe		
Outside	Inside	Coating
Good ☐	☐	☐
Fair ☐	☐	☐
Bad ☐	☐	☐
Anode #	MV Reading	

Existing Main	
Size 4"	Pressure Type/Mfr Dura Line
Lot #	Cover 36" Location
New Service / Main	
Size 1"	Lot # NAD164033GB 17 Feb
Poly Mfr Dura Line	Nature of Soil C/41
Tap Size 1/2	Cover 36" Completion Date 9/20/13
Foreman ID T. Schanham	Welder/Fuser ID T. Schanham
Pressure Test	
Test With: Air / Nitrogen	Duration 15min Emp ID T. Schanham
Date Tested 9/20/13	PSI 150 Soap Test Final Tie-in? Y ☒ N ☐
Filled out by Mapping Dept.	
Mapped in System Maps	Date
Mapped in GIS	Date
Entry Person	Date
GSOC Polygon Available	Yes No

Description	Install Footage
Directional Bore	
Pneumatic Bore	45'
Backhoe	28'
Inserting	
Trench	
Plow	108'
Hand Digging	
Splitting	
Joint Trench	
Gopher Pipe	
Cust. Perf. Loc.	
